

Untitled Gantt Project

Apr 29, 2020

<http://>

Project manager

Project dates

Jun 16, 2020 - Aug 25, 2020

Completion

0%

Tasks

58

Resources

0

Tasks

Name	Begin date	End date
2 Week Return Notic	6/16/20	6/29/20
2 Week Restore Period	6/30/20	7/13/20
Lock Ups	6/30/20	7/13/20
CEBAF Open	6/30/20	6/30/20
INJ Locked Up	7/1/20	7/13/20
NL Locked Up	7/2/20	7/13/20
SL/BSY Lock Up	7/3/20	7/13/20
Hall A Lock Up	7/8/20	7/8/20
Hall B Lock Up	7/8/20	7/8/20
Hall C Lock Up	7/8/20	7/8/20
Hall D Lock Up	7/8/20	7/8/20
Cryo	6/28/20	7/3/20
4.5k Reroute for Repair	6/28/20	6/29/20
Pull 4.5k Return Bypass U Tube	6/30/20	6/30/20
INJ/NL Pumpdown Start	7/1/20	7/1/20
<i>Start filling INJ/C100 Modules First</i>		
<i>Reinstall 4.5k U Tube</i>		
SL/LERF Pumpdown	7/2/20	7/2/20
<i>Finish filling INJ/NL</i>		
<i>Start filling C100's</i>		
Pumpdown/Filling Complete	7/3/20	7/3/20
<i>Pumpdown and Filling Complete</i>		
SSG	6/30/20	7/8/20
SA Camera Fix	6/30/20	6/30/20
Sweep Changes	7/1/20	7/1/20
MBSY1C Troubleshooting	7/8/20	7/8/20


Tasks

Name	Begin date	End date
EES IC	6/30/20	7/1/20
Standard HCO	6/30/20	7/1/20
EES RF	6/30/20	7/5/20
Repairs and HCO	6/30/20	7/1/20
INJ/NL Recovery	7/2/20	7/3/20
Separator Recovery	7/3/20	7/3/20
SL Recovery	7/3/20	7/4/20
Energy Push	7/4/20	7/5/20
Installation	6/30/20	7/1/20
Tunnel Walkthrough	6/30/20	6/30/20
<i>Checking and fixing water leaks</i>		
HCO	7/1/20	7/1/20
EES DC	6/30/20	7/8/20
Inspections and INJ Trims	6/30/20	6/30/20
Main Machine Trims	7/1/20	7/3/20
ARC Box Supply Restore	7/3/20	7/4/20
Hall Power Supplies	7/8/20	7/8/20
SRF	7/2/20	7/2/20
1L25 FE Measurements	7/2/20	7/2/20
Facilities	6/30/20	7/1/20
Belt/Filter Repairs	6/30/20	7/1/20
Gun	6/30/20	7/1/20
Reactivate Cathode	6/30/20	7/1/20

Tasks

Name	Begin date	End date
Cathode Rotatation (PQB) <i>After heat and reactivation of cathode. PQB folks and CIS will need some time to realign the cathode rotation.</i>	7/1/20	7/1/20
Beam Ops	7/2/20	7/14/20
Warm RF INJ	7/2/20	7/2/20
INJ Restore	7/3/20	7/4/20
PQB Verification	7/4/20	7/4/20
Beam to 5C	7/5/20	7/6/20
Arc1 M5,6	7/7/20	7/7/20
Rematch to 2R	7/8/20	7/8/20
Beam to 4R	7/9/20	7/9/20
Beam to 6R	7/10/20	7/10/20
Assess 7S BComm Setting	7/10/20	7/10/20
Beam to 8R	7/11/20	7/11/20
Beam to 5C	7/12/20	7/12/20
Tuning to Halls	7/13/20	7/14/20
6 Weeks Physics	7/14/20	8/24/20

Gantt Chart

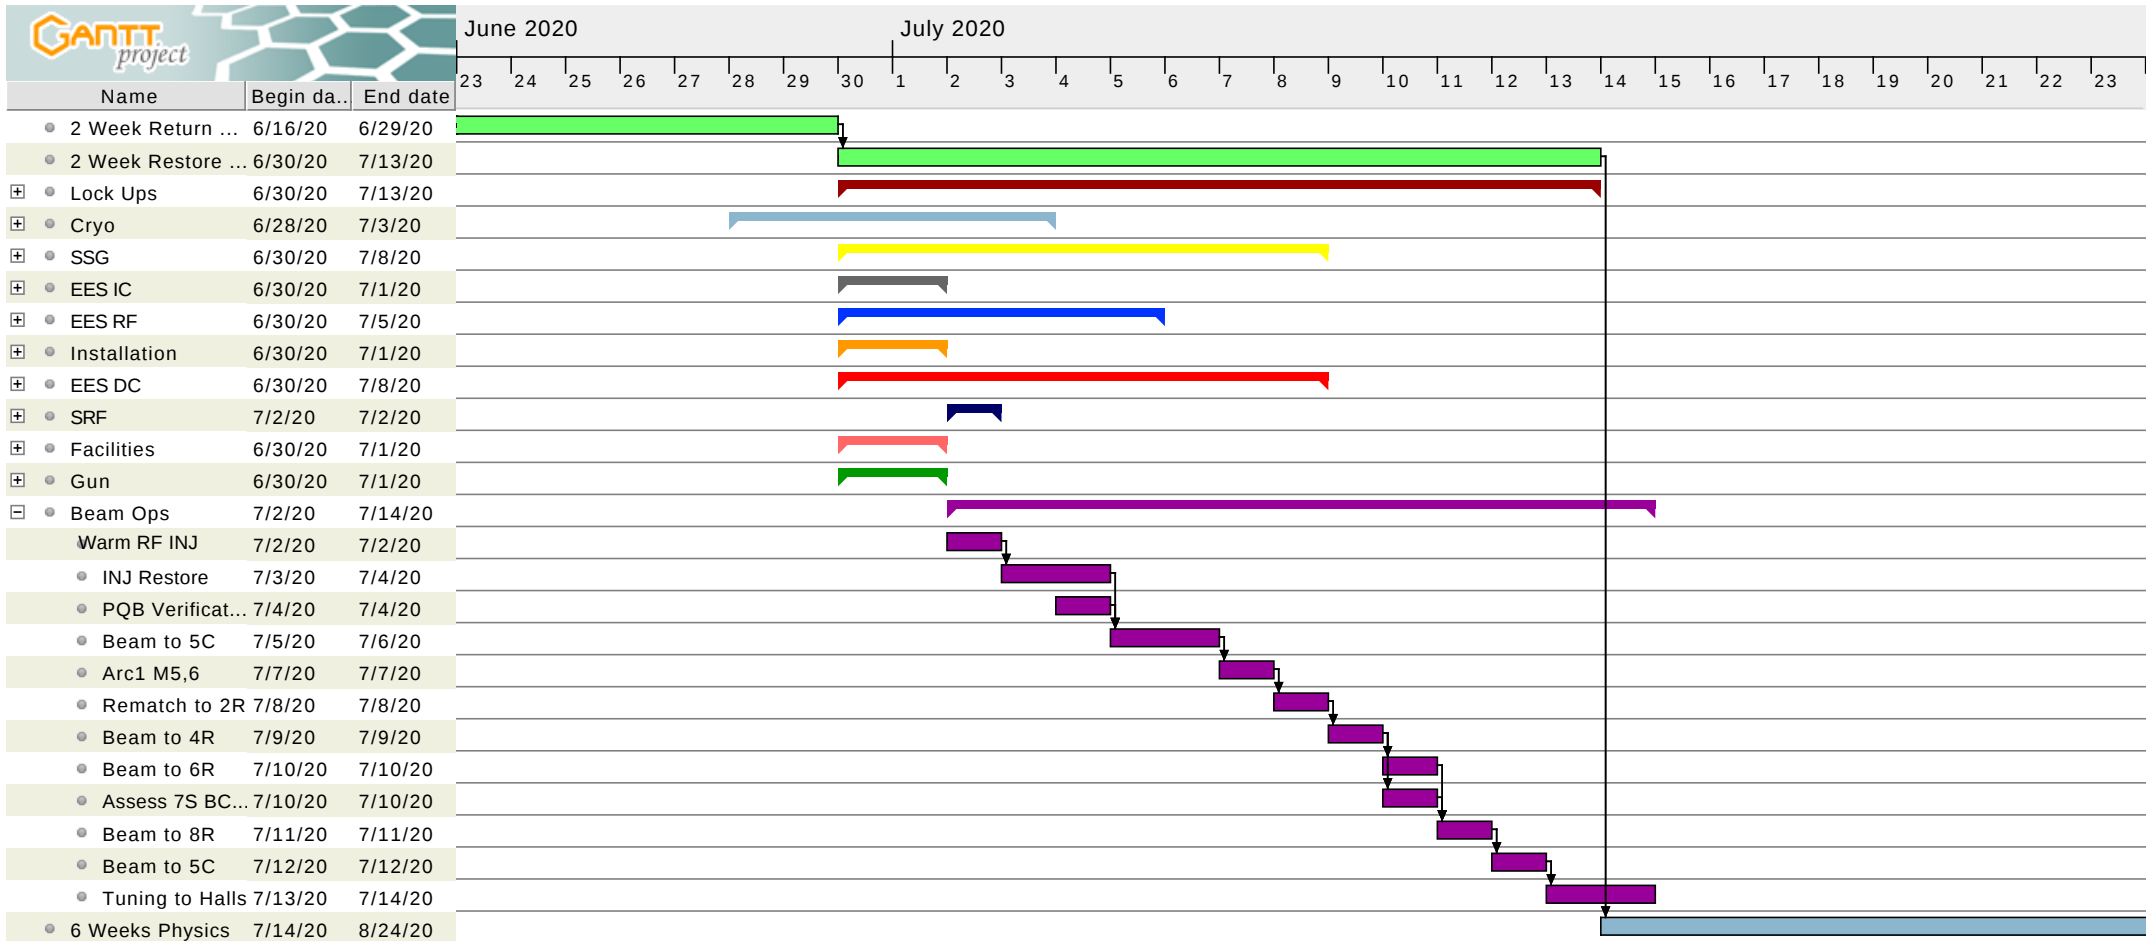

Resources Chart

